


HONEYTOWN ROAD BRIDGE

BRIDGE No: CAN-TR 54-1.82



SOUTH APPROACH

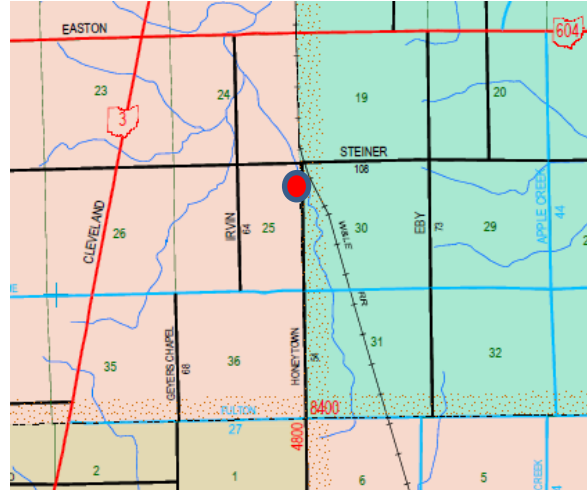

ELEVATION

LOCATION: Honeytown Road over Br. of Chippewa; 0.2 Mile South of Steiner Rd. (CR 108)

EXISTING STRUCTURE: Single-Span Concrete Slab and Spread Footing Concrete Abutments
Deck Width = 16.7' Toe to Toe of Concrete Railing

PROPOSED STRUCTURE: 16' x 7' x 52'-0" Concrete Box Culvert.
Deck Width = 24'-0" Face to Face Railing

PROJECT FINANCING: Force Account (Local K-Funds; Auto License & Gas Tax Funds)

ESTIMATED COST: \$101,445.00

REASON: Structurally Deficient

CONTRACTOR: County Crew
